


Appendix A

Master Programme

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility

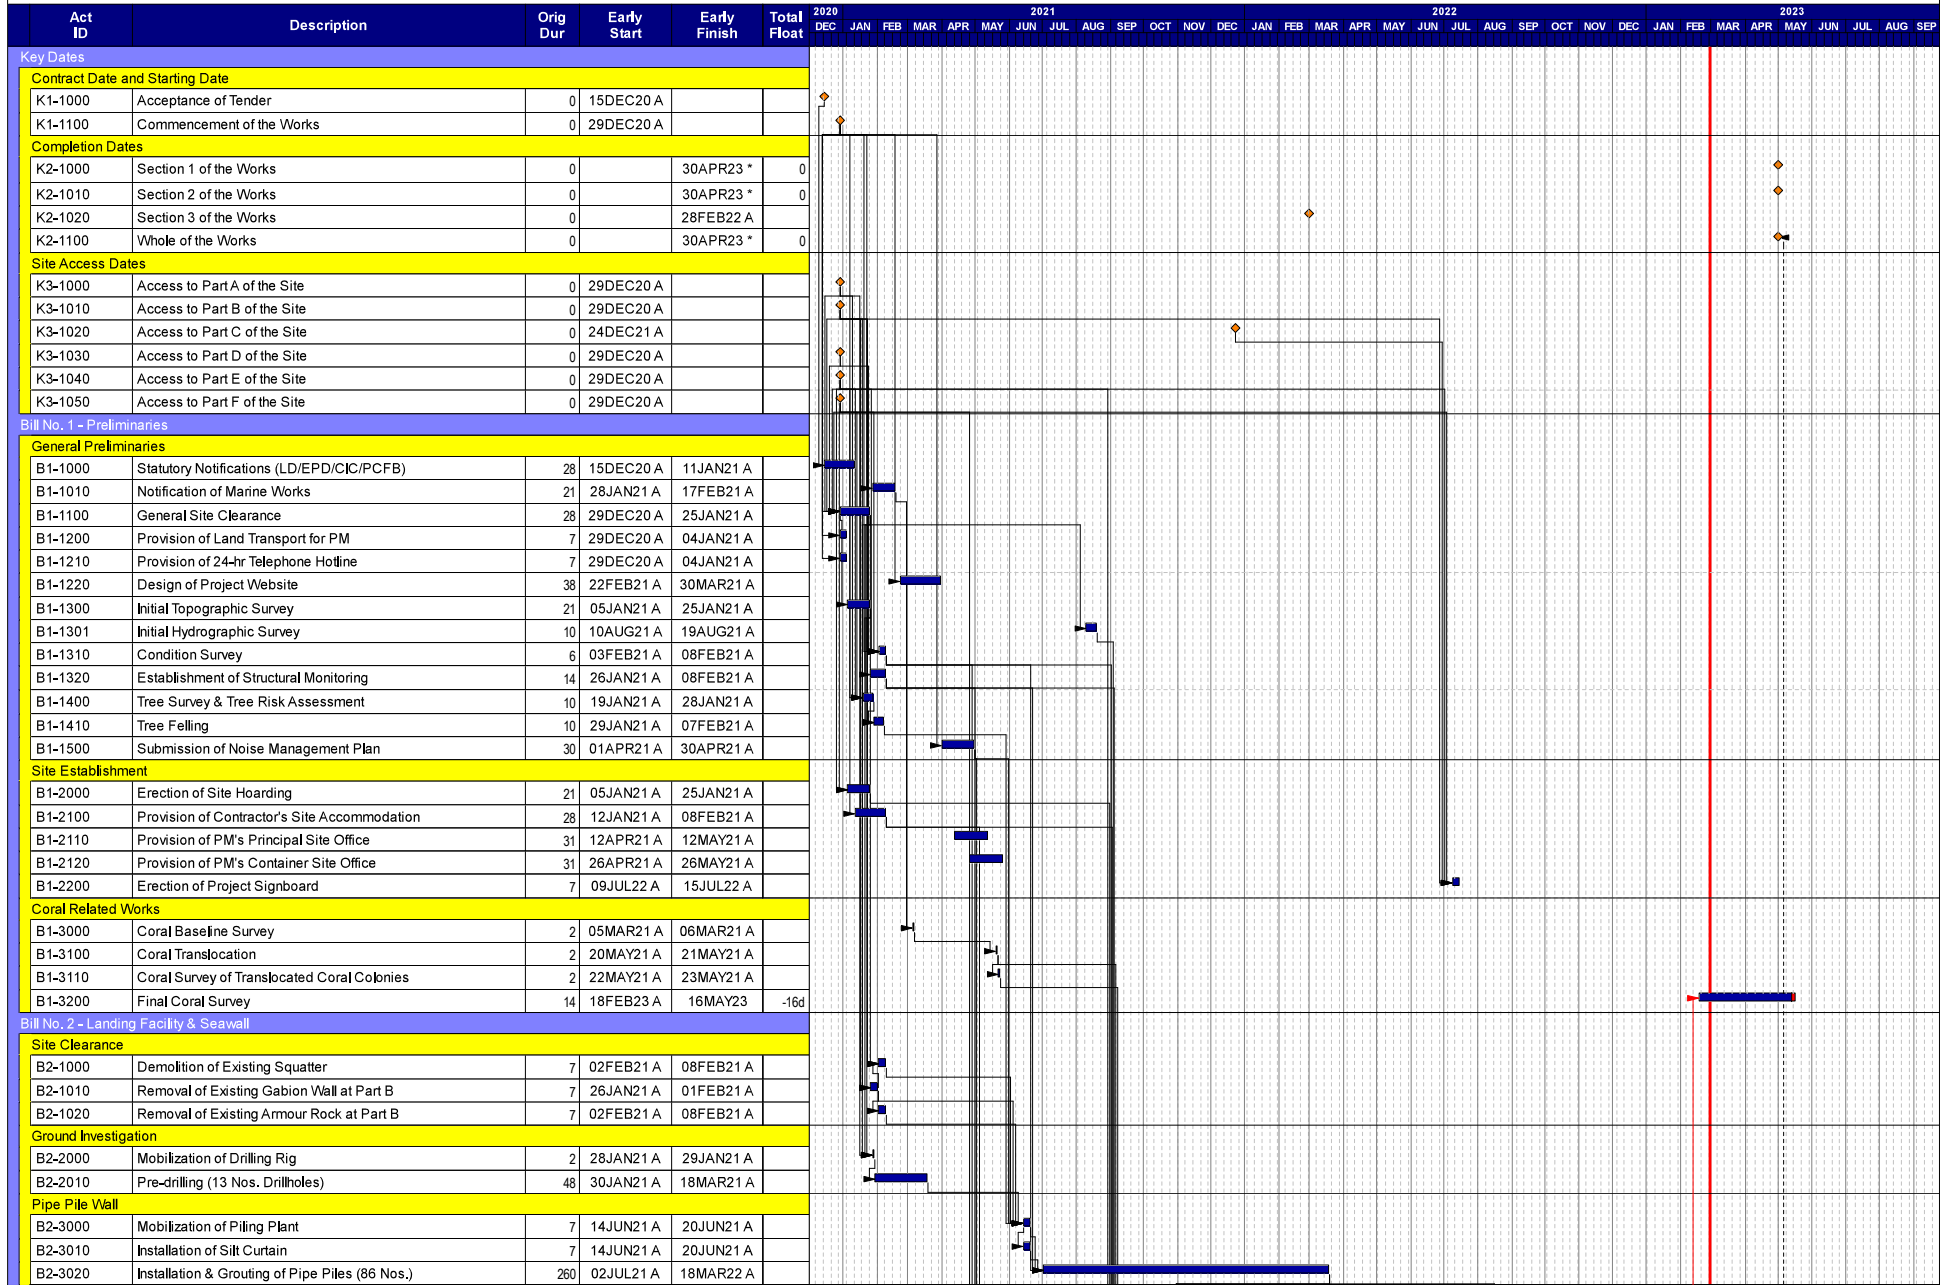

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility

Act ID	Description	Orig Dur	Early Start	Early Finish	Total Float	2020												2021												2022												2023											
						DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP		
Bill No. 3 - Breakwater																																																					
Ground Investigation																																																					
B3-2000	Mobilization of Drilling Rig & Jackup Barge	3	08JUN21 A	10JUN21 A																																																	
B3-2010	Pre-drilling (8 Nos. Drillholes)	33	11JUN21 A	13JUL21 A																																																	
Temporary Working Platform																																																					
B3-1000	Installation of Silt Curtain	3	04NOV21 A	06NOV21 A																																																	
B3-1100	Submission of Temporary Works Design	54	11OCT21 A	03DEC21 A																																																	
B3-1200	Installation of Temporary Piles	24	28DEC21 A	20JAN22 A																																																	
B3-1210	Installation of Temporary Working Platform	30	31DEC21 A	29JAN22 A																																																	
Socketted Steel H-piles																																																					
B3-3000	Mobilization of Piling Plant	7	11MAR22 A	17MAR22 A																																																	
B3-3010	Construction of Preliminary Piles	23	24MAR22 A	15APR22 A																																																	
B3-3020	Construction of Main Piles (34 Nos.)	113	16APR22 A	06AUG22 A																																																	
B3-3100	Setup of Pile Testing Equipment	5	06JUL22 A	10JUL22 A																																																	
B3-3110	Pile Load Test (2 Nos.)	20	11JUL22 A	30JUL22 A																																																	
Breakwater Structure																																																					
B3-4000	Modification of Temporary Working Platform	28	01SEP22 A	28SEP22 A																																																	
B3-4010	Modification of Pile Heads (PMI No.55)	80	21NOV22 A	08FEB23 A																																																	
B3-4100	Cast In-situ Pile Caps (PB14 & PB15)	120	28OCT22 A	28FEB23 A																																																	
B3-4110	Cast In-situ Breakwater Tip Pile Cap (BW2)	18	28FEB23	17MAR23	-87d																																																
B3-4120	Protective Coating on Pile Caps	18	18MAR23	04APR23	-63d																																																
B3-4200	Installation of Precast Frame Units (BW1 x 10)	14	29APR23	12MAY23	-87d																																																
B3-4210	Installation of Precast Frame Unit (BW3)	7	03JUN23	09JUN23	-53d																																																
B3-4400	Removal of Temporary Working Platform	14	18MAR23	31MAR23	30d																																																
Ancillary Works																																																					
B3-5100	Installation of Navigation Light Post	10	10JUN23	19JUN23	-53d																																																
B3-5200	Vacation of Site Area	3	20JUN23	22JUN23	-53d																																																
Bill No. 4 - Lookout Point and Viewing Platform																																																					
Improvement Works at Lookout Point																																																					
B4-1000	Demolition of Existing Wall	7	10MAY21 A	16MAY21 A																																																	
B4-1100	Levelling of Existing Beach	14	17MAY21 A	31MAY21 A																																																	
B4-1200	Mobilization of Piling Plant	4	07JUN21 A	10JUN21 A																																																	
B4-1210	Installation of Pipe Piles (40 Nos.)	74	11JUN21 A	23AUG21 A																																																	
B4-1220	Trimming of Pipe Piles for Wall Openings	7	10SEP21 A	16SEP21 A																																																	
B4-1230	Infill Grouting of Pipe Piles	7	09OCT21 A	06NOV21 A																																																	
B4-1280	Demobilization and Site Preparation	21	28NOV21 A	18DEC21 A																																																	
B4-1290	Excavation and Placing of Concrete Blinding	24	28DEC21 A	20JAN22 A																																																	
B4-1300	Casting of Skin Wall	37	28JAN22 A	05MAR22 A																																																	
B4-1400	Laying of Concrete Paving	0	13MAR22 A	19MAR22 A																																																	
Improvement Works at Viewing Platform																																																					
B4-2000	Relocation of Existing Gabion Blocks	6	10SEP21 A	15SEP21 A																																																	
B4-2010	Temporary Modification of Existing Drainage	29	18AUG21 A	15SEP21 A																																																	
B4-2100	Mobilization of Piling Plant	7	16SEP21 A	22SEP21 A																																																	
B4-2110	Installation of Pipe Piles (30 Nos.)	47	25OCT21 A	10DEC21 A																																																	
B4-2120	Infill Grouting of Pipe Piles	6	11DEC21 A	16DEC21 A																																																	
B4-2130	Demobilization and Site Preparation	10	17DEC21 A	26DEC21 A																																																	
B4-2200	Excavation to Formation Level	20	19JAN22 A	07FEB22 A																																																	
B4-2210	Placing of Levelling Stones	2	08FEB22 A	09FEB22 A																																																	
B4-2219	Precasting of Seawall Blocks	35	22DEC21 A	25JAN22 A																																																	
B4-2220	Installation of Seawall Blocks	2	10FEB22 A	11FEB22 A																																																	
B4-2221	Precasting of Concrete Backing w/ Granite Facing	39	22DEC21 A	29JAN22 A																																																	
B4-2230	Placing of Concrete Blinding	2	21FEB22 A	22FEB22 A																																																	
B4-2240	Installation of Concrete Backing	2	21FEB22 A	22FEB22 A																																																	
B4-2250	Cast in-situ Concrete Coping	8	01MAR22 A	08MAR22 A																																																	

