


Appendix A

Master Programme

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility

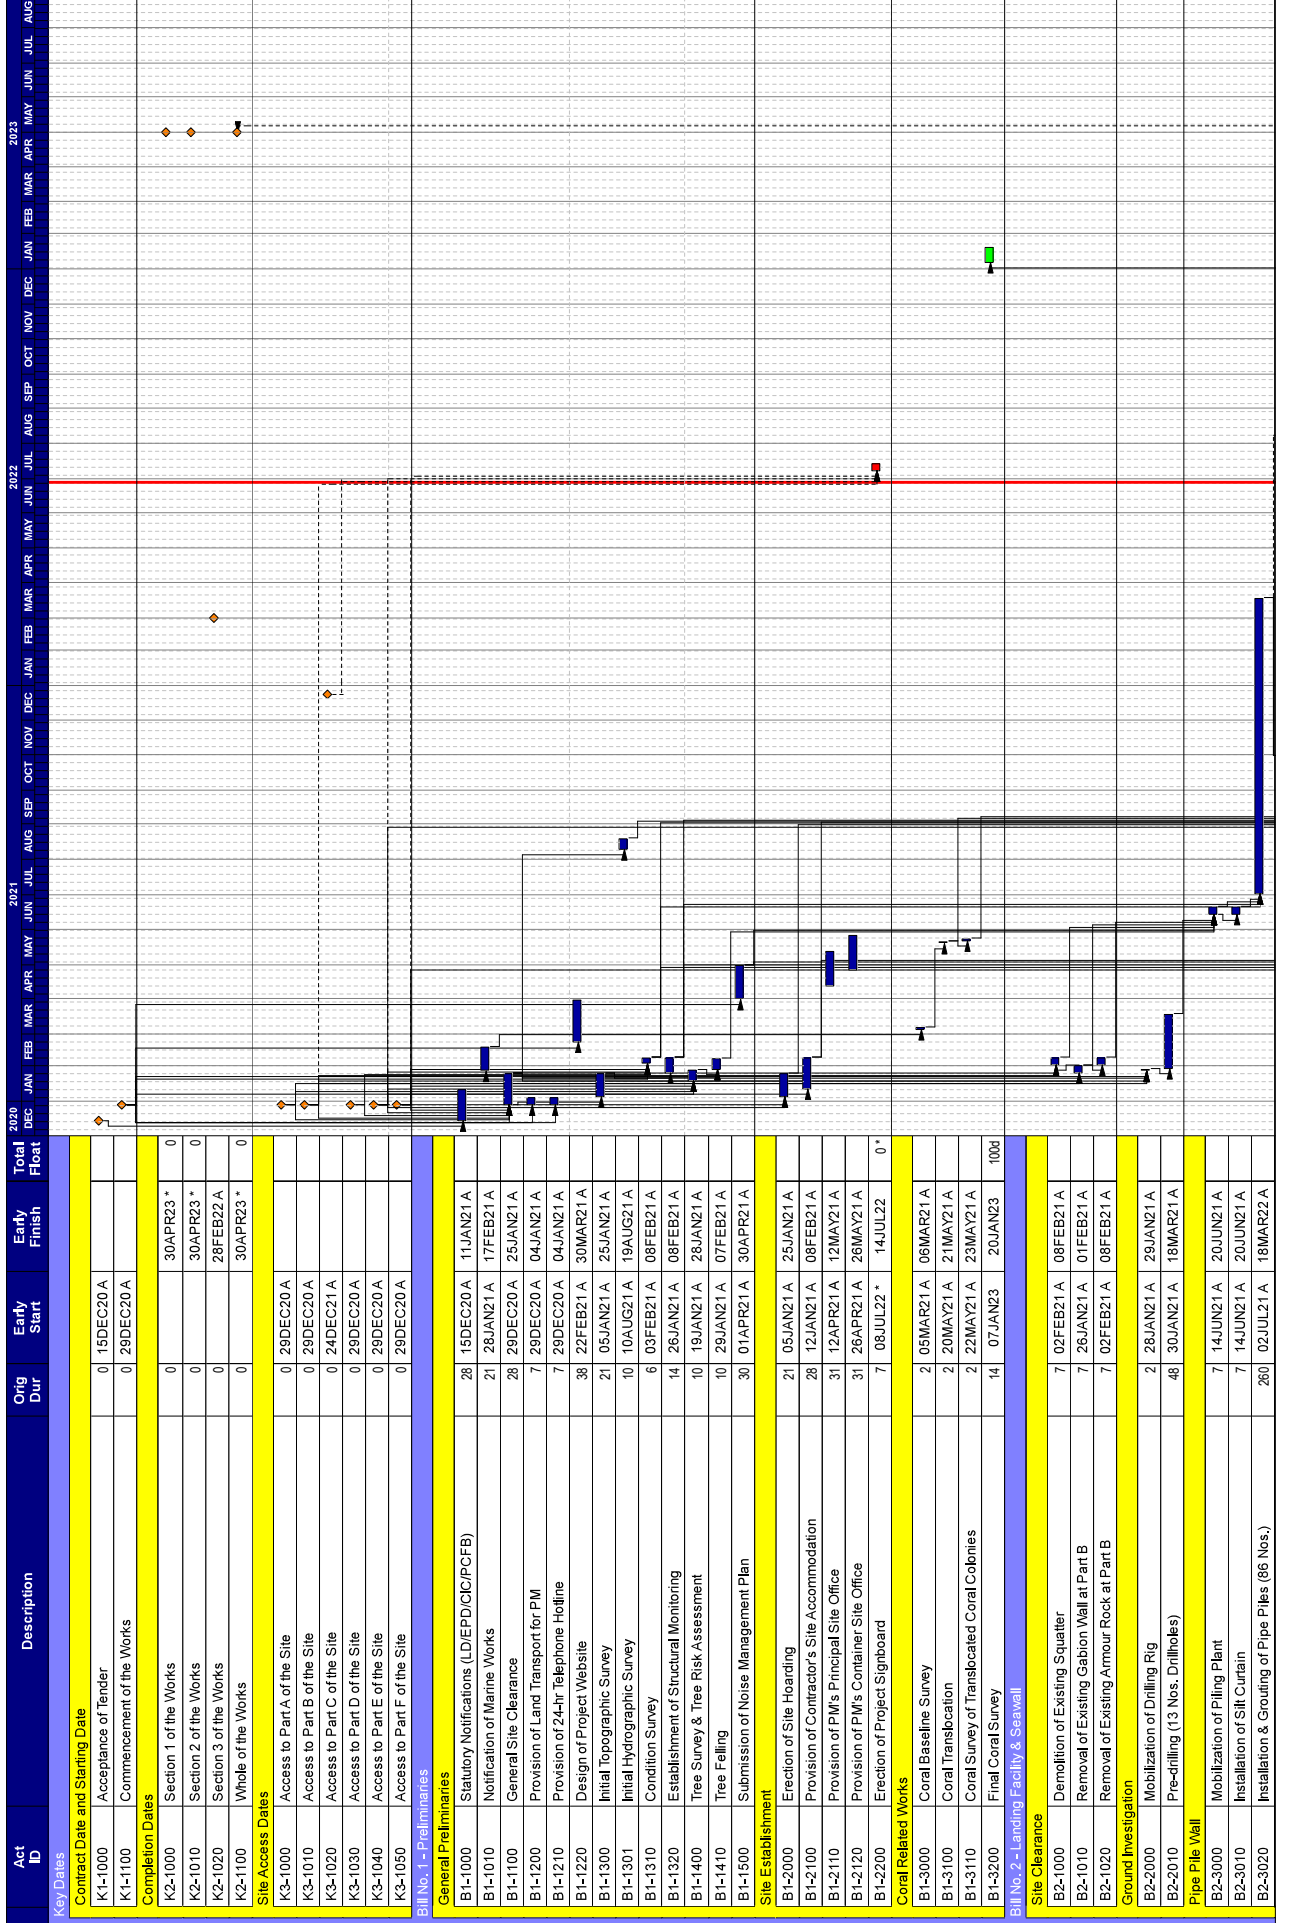


Act ID	Description	Orig Dur	Early Start	Early Finish	Total Float
--------	-------------	----------	-------------	--------------	-------------


Key Dates					
Contract Date and Standing Date					
K1-1000	Acceptance of Tender	0	15DEC20 A		
K1-1100	Commencement of the Works	0	29DEC20 A		
Completion Dates					
K2-1000	Section 1 of the Works	0		30APR23 *	0
K2-1010	Section 2 of the Works	0		30APR23 *	0
K2-1020	Section 3 of the Works	0		28FEB22 A	
K2-1100	Whole of the Works	0		30APR23 *	0
Site Access Dates					
K3-1000	Access to Part A of the Site	0	29DEC20 A		
K3-1010	Access to Part B of the Site	0	29DEC20 A		
K3-1020	Access to Part C of the Site	0	24DEC21 A		
K3-1030	Access to Part D of the Site	0	29DEC20 A		
K3-1040	Access to Part E of the Site	0	29DEC20 A		
K3-1050	Access to Part F of the Site	0	29DEC20 A		

Bill No. 1 - Preliminaries					
General Preliminaries					
B1-1000	Statutory Notifications (LDEPD/CIC/PCFB)	28	15DEC20 A	11JAN21 A	
B1-1010	Notification of Marine Works	21	28JAN21 A	17FEB21 A	
B1-1100	General Site Clearance	28	29DEC20 A	25JAN21 A	
B1-1200	Provision of Land Transport for PM	7	29DEC20 A	04JAN21 A	
B1-1210	Provision of 24-hr Telephone Hotline	7	29DEC20 A	04JAN21 A	
B1-1220	Design of Project Website	38	22FEB21 A	30MAR21 A	
B1-1300	Initial Topographic Survey	21	05JAN21 A	25JAN21 A	
B1-1301	Initial Hydrographic Survey	10	10AUG21 A	19AUG21 A	
B1-1310	Condition Survey	6	03FEB21 A	09FEB21 A	
B1-1320	Establishment of Structural Monitoring	14	26JAN21 A	09FEB21 A	
B1-1400	Tree Survey & Tree Risk Assessment	10	19JAN21 A	28JAN21 A	
B1-1410	Tree Felling	10	29JAN21 A	07FEB21 A	
B1-1500	Submission of Noise Management Plan	30	01APR21 A	30APR21 A	
Site Establishment					
B1-2000	Erection of Site Hoarding	21	05JAN21 A	25JAN21 A	
B1-2100	Provision of Contractor's Site Accommodation	28	12JAN21 A	09FEB21 A	
B1-2110	Provision of PM's Principal Site Office	31	12APR21 A	12MAY21 A	
B1-2120	Provision of PM's Container Site Office	31	26APR21 A	26MAY21 A	
B1-2200	Erection of Project Signboard	7	08JUL22 *	14JUL22 *	0 *
Coral Related Works					
B1-3000	Coral Baseline Survey	2	05MAR21 A	06MAR21 A	
B1-3100	Coral Translocation	2	20MAY21 A	21MAY21 A	
B1-3110	Coral Survey of Translocated Coral Colonies	2	22MAY21 A	23MAY21 A	
B1-3200	Final Coral Survey	14	07JAN23	20JAN23	100d
Bill No. 2 - Landing Facility & Seawall					
Site Clearance					
B2-1000	Demolition of Existing Squatter	7	02FEB21 A	09FEB21 A	
B2-1010	Removal of Existing Gabion Wall at Part B	7	26JAN21 A	01FEB21 A	
B2-1020	Removal of Existing Armour Rock at Part B	7	02FEB21 A	09FEB21 A	
Ground Investigation					
B2-2000	Mobilization of Drilling Rig	2	28JAN21 A	29JAN21 A	
B2-2010	Pre-drilling (13 Nos. Drillholes)	48	30JAN21 A	18MAR21 A	
Pipe Pile Wall					
B2-3000	Mobilization of Piling Plant	7	14JUN21 A	20JUN21 A	
B2-3010	Installation of Silt Curtain	7	14JUN21 A	20JUN21 A	
B2-3020	Installation & Grouting of Pipe Piles (86 Nos.)	280	02JUL21 A	18MAR22 A	

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility

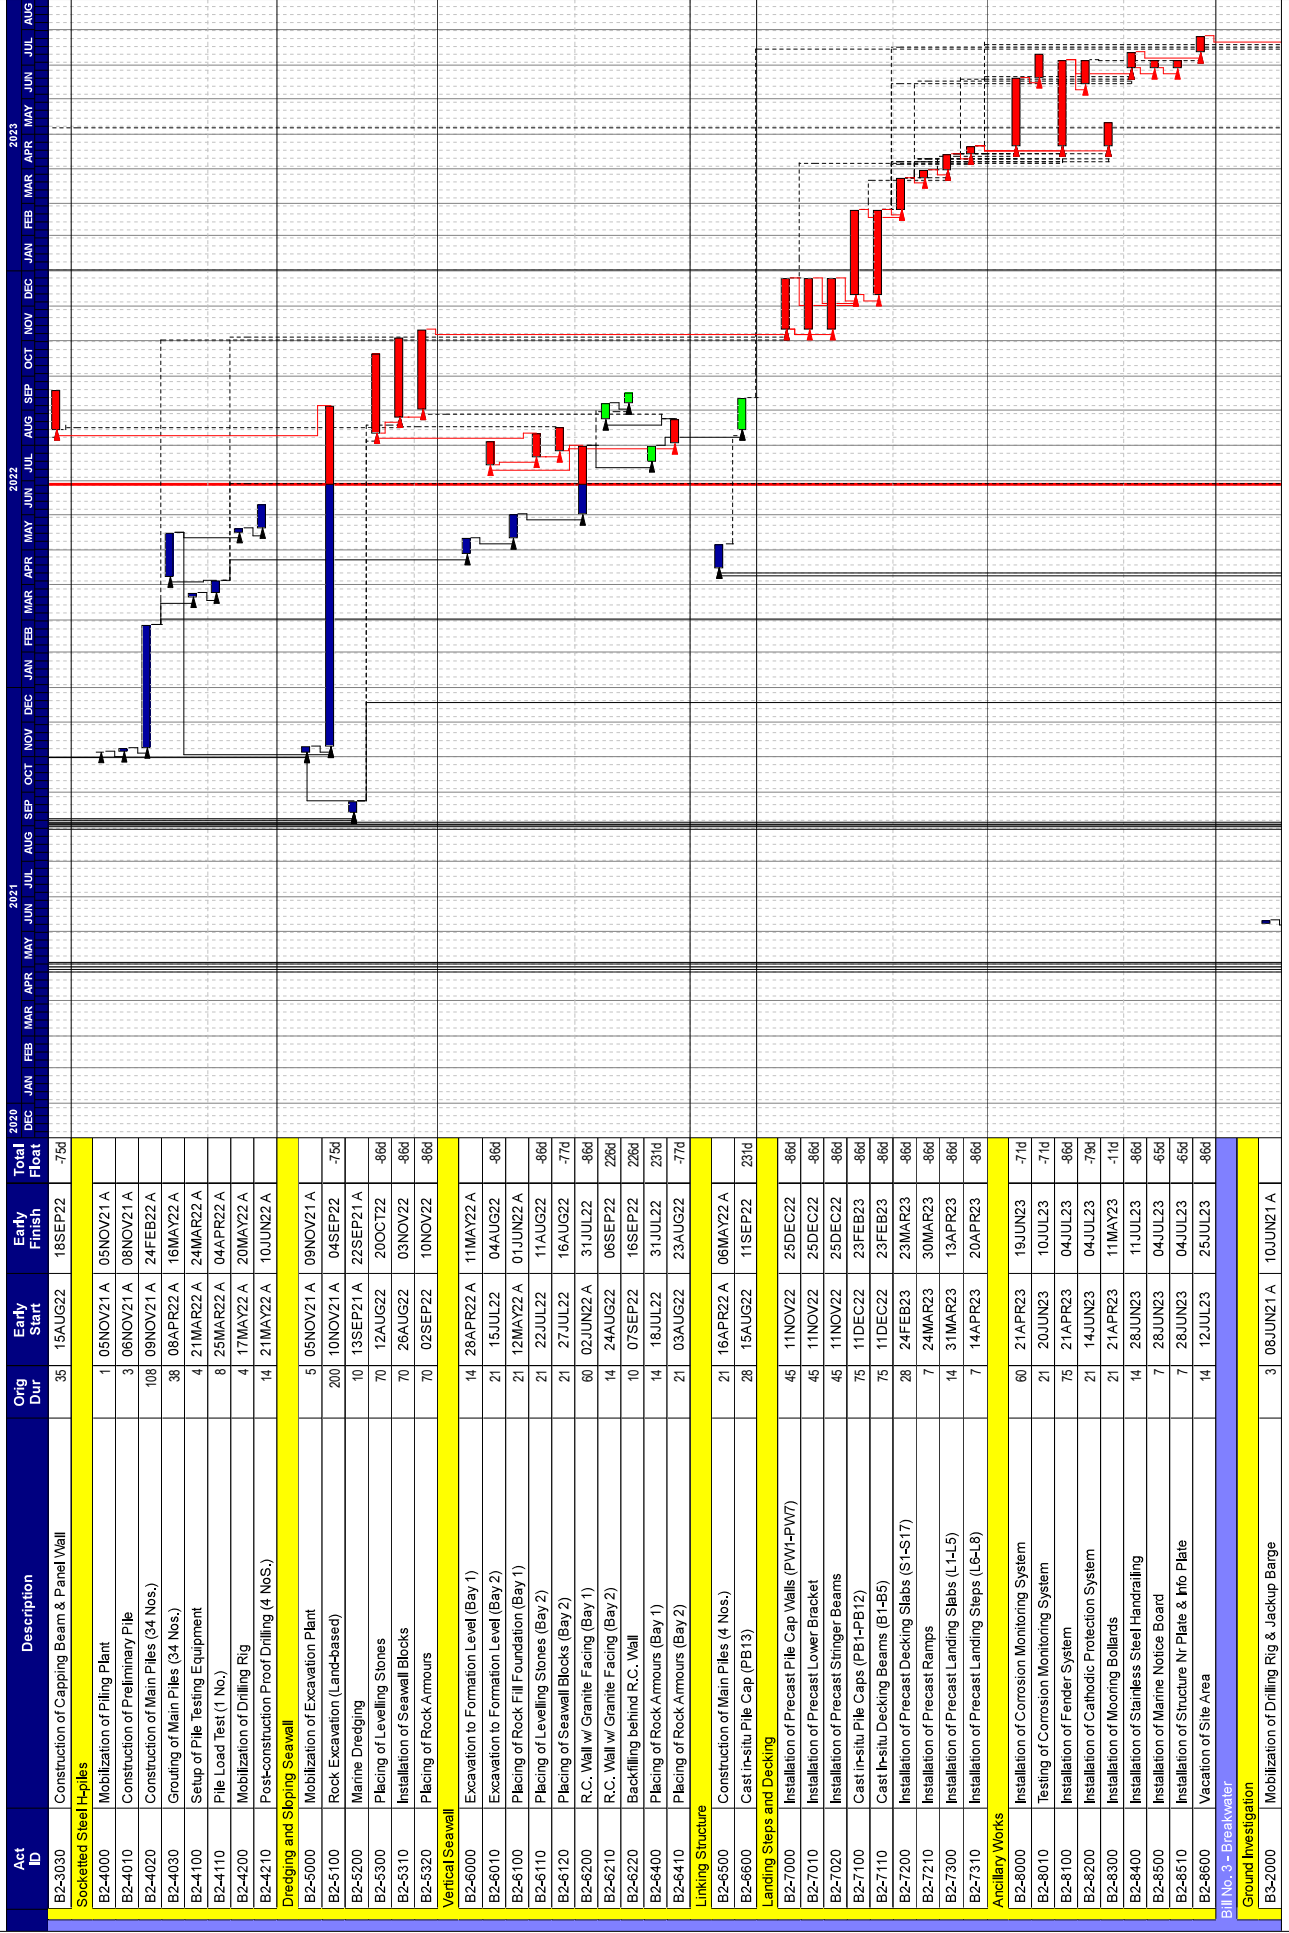

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility

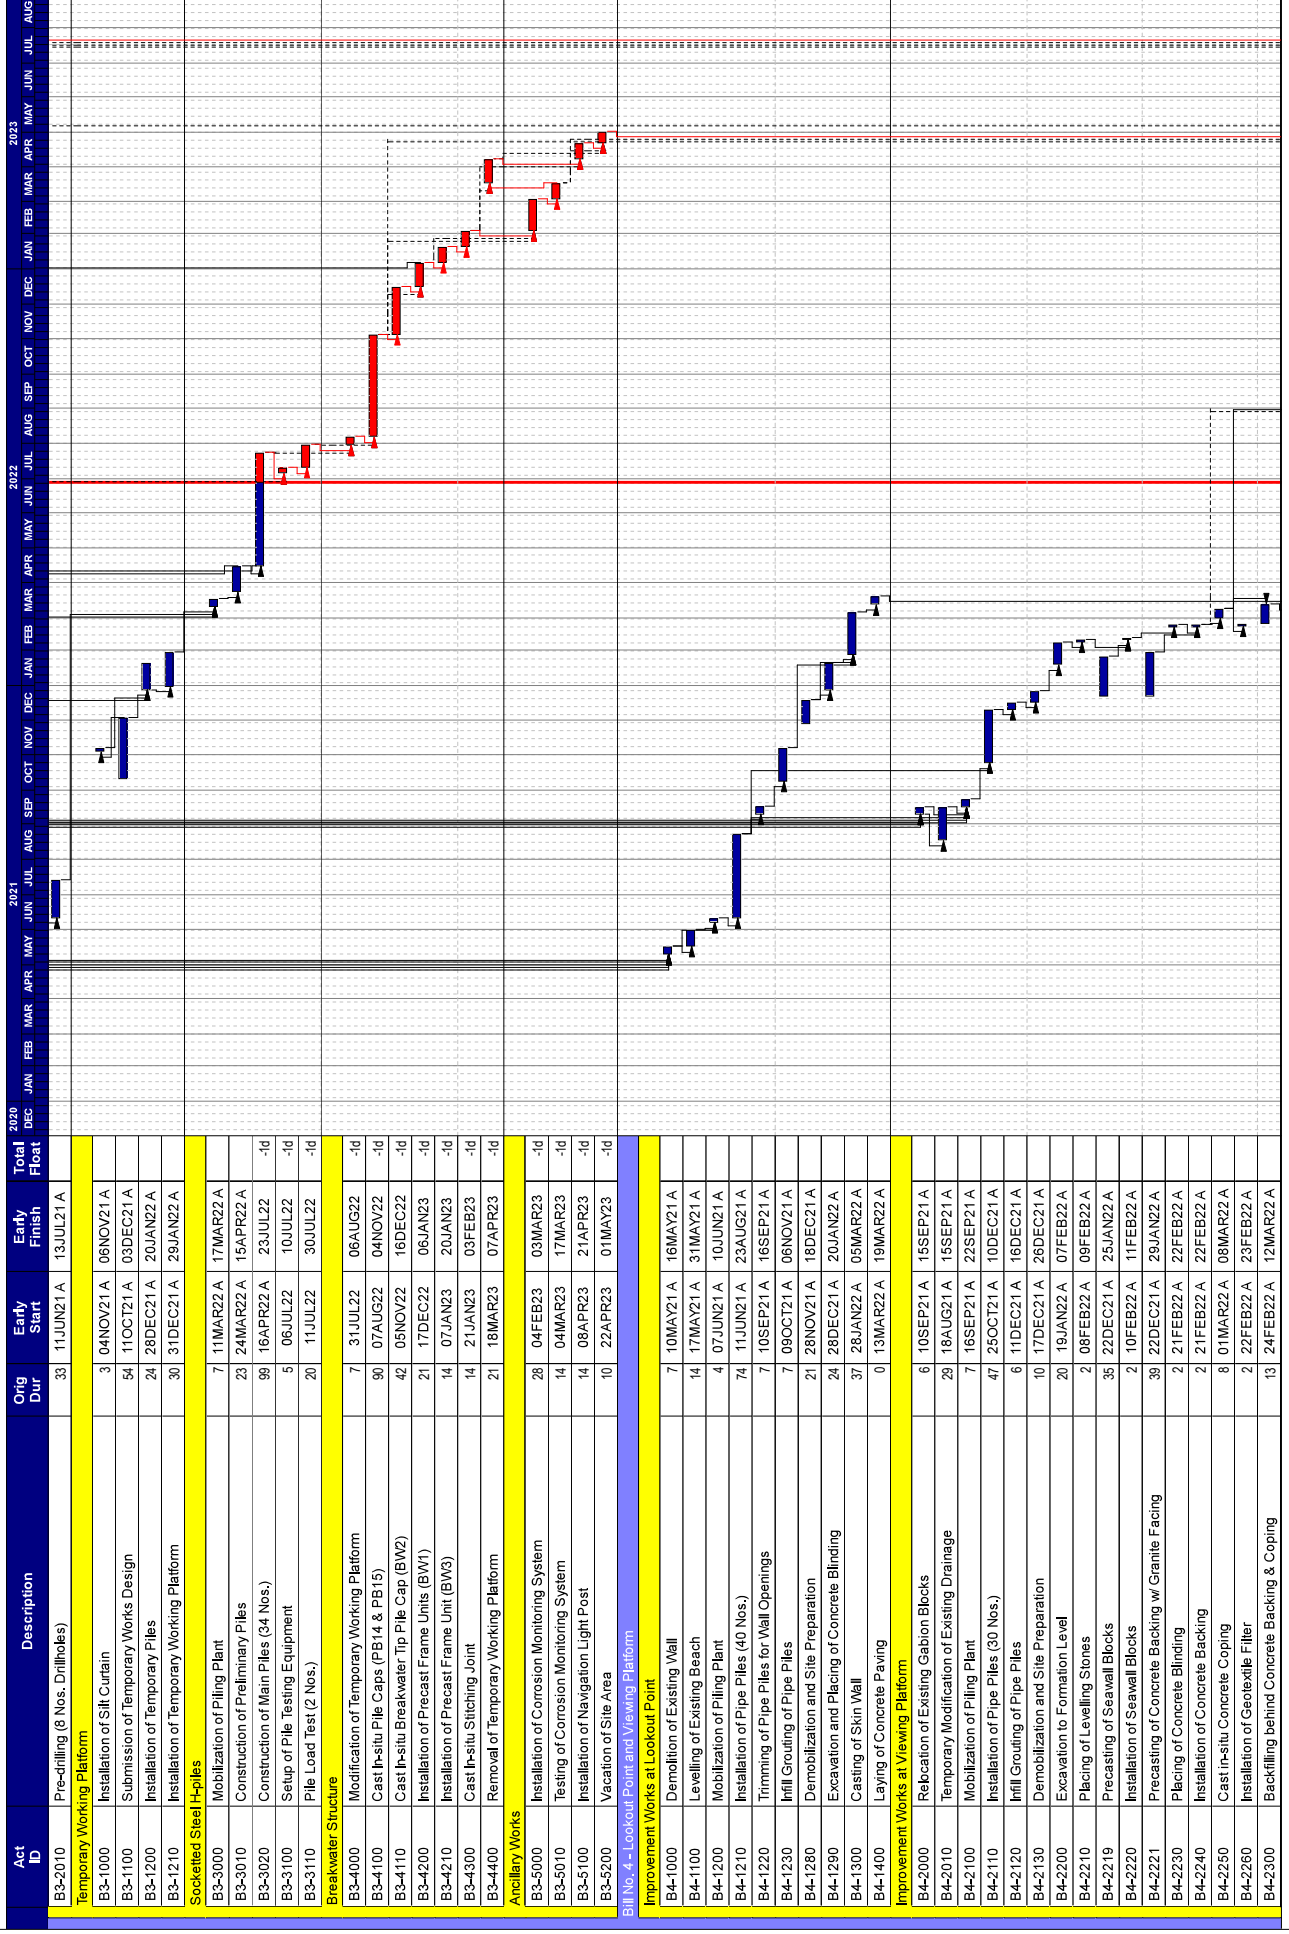

SS J521

SSJ521- Short Term Program for Completion

		Items	oustanding	day	Completed date
1	concrete works	viewing platform and its kerb	√	14	8/8/2022
		concrete ramp to beach	√	12	15/8/2022
		backfill and modify beach profile	√	7	30/8/2022
2	metal works	all structural steel works	√	30	23/8/2022
		all balustrades	√	21	13/8/2022
		alu panel	√	21	23/8/2022
		garden handrails	√	14	10/8/2022
		painting touch up	√	10	23/8/2022
3	finishes	viewing platform - grano	√	14	18/8/2022
		viewing platform - floor tiling	√	40	26/8/2022
		garden - grano	√	14	18/8/2022
		meter room painting	√	4	5/8/2022
4	drainage	all ug manhole and duct	√	10	5/8/2022
		channel cover	√	7	16/8/2022
		matching cover	√	7	16/8/2022
5	equipment	braille map	√	150	Dec-22
		garden signage	√	30	16/8/2022
		playground equipment	√	7	10/8/2022
		pergola top	√	14	10/8/2022
		safety mat	√	7	19/8/2022
6	landscape	outside site boundary	√	7	12/8/2022
		within site boundary	√	7	19/8/2022
7	BS installation	wind turbine installation	√	10	12/8/2022
		all lighting	√	14	19/8/2022
		all plumbing	√	14	19/8/2022
8	clearance	water barrier removal	√	3	6/9/2022
		concrete hoarding removal	√	7	9/9/2022
