

Appendix A

Master Programme

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility

Act ID	Description	Orig Dur	Early Start	Early Finish	Total Float	2021				2022										
						DEC				JAN		FEB		MAR		APR				
						06	13	20	27	03	10	17	24	31	07	14	21	28	07	14
Key Dates																				
Completion Dates																				
K2-1020	Section 3 of the Works	0		28FEB22 *	0															
Bill No. 1 - Preliminaries																				
Site Establishment																				
B1-2200	Erection of Project Signboard	21	31DEC21	20JAN22	0 *															
Bill No. 2 - Landing Facility & Seawall																				
Pipe Pile Wall																				
B2-3020	Installation & Grouting of Pipe Piles (86 Nos.)	200	02JUL21 A	17JAN22	-16d															
Socketted Steel H-piles																				
B2-4020	Construction of Main Piles (34 Nos.)	84	09NOV21 A	31JAN22	-45d															
B2-4100	Setup of Pile Testing Equipment	14	08FEB22	21FEB22	105d															
B2-4110	Pile Load Test (1 No.)	4	22FEB22	25FEB22	105d															
B2-4200	Mobilization of Drilling Rig	4	15FEB22	18FEB22	23d															
B2-4210	Post-construction Proof Drilling (1 No.)	7	19FEB22	25FEB22	23d															
Dredging and Sloping Seawall																				
B2-5100	Rock Excavation (Land-based)	160	10NOV21 A	18APR22	-29d															
Linking Structure																				
B2-6500	Construction of Main Piles (4 Nos.)	21	08MAR22	28MAR22	74d															
Bill No. 3 - Breakwater																				
Temporary Working Platform																				
B3-1200	Installation of Temporary Piles	10	28DEC21	06JAN22	-33d															
B3-1210	Installation of Temporary Working Platform	28	31DEC21 A	19JAN22	-33d															
Socketted Steel H-piles																				
B3-3000	Mobilization of Piling Plant	14	08FEB22	21FEB22	-45d															
B3-3010	Construction of Preliminary Pile	14	22FEB22	07MAR22	-45d															
B3-3020	Construction of Main Piles (34 Nos.)	140	08MAR22	25JUL22	-45d															
Bill No. 4 - Lookout Point and Viewing Platform																				
Improvement Works at Lookout Point																				
B4-1290	Excavation and Placing of Concrete Blinding	11	28DEC21	07JAN22	24d															
B4-1300	Casting of Skin Wall	14	08JAN22	21JAN22	24d															
B4-1400	Laying of Concrete Paving	14	22JAN22	04FEB22	24d															
Improvement Works at Viewing Platform																				
B4-2200	Excavation to Formation Level	10	05JAN22	14JAN22	-20d															
B4-2210	Placing of Levelling Stones	7	15JAN22	21JAN22	-20d															
B4-2219	Precasting of Seawall Blocks	21	22DEC21 A	11JAN22	-10d															
B4-2220	Installation of Seawall Blocks	3	22JAN22	24JAN22	-20d															

CEDD Contract No. CV/2020/09
Construction of Lei Yue Mun Public Landing Facility


Act ID	Description	Orig Dur	Early Start	Early Finish	Total Float	2021							2022													
						DEC							JAN			FEB				MAR			APR			
						06	13	20	27	03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25
B4-2221	Precasting of Concrete Backing w/ Granite Facing	32	22DEC21 A	22JAN22	-15d																					
B4-2230	Placing of Concrete Blinding	2	25JAN22	26JAN22	-20d																					
B4-2240	Installation of Concrete Backing	3	28JAN22	30JAN22	-20d																					
B4-2250	Cast in-situ Concrete Coping	12	07FEB22	18FEB22	-20d																					
B4-2260	Installation of Geotextile Filter	4	19FEB22	22FEB22	-20d																					
B4-2300	Backfilling behind Concrete Backing & Coping	14	23FEB22	08MAR22	-20d																					
B4-2400	Installation of Enhanced Seawall Panels	14	26FEB22	11MAR22	-16d																					
B4-2500	Laying of Concrete Paving	7	09MAR22	15MAR22	-20d																					
B4-2600	Vacation of Site Area	5	16MAR22	20MAR22	-20d																					
Completion and Handover																										
Sectional Completion																										
C1-1020	Completion of Section 3 of the Works	0		20MAR22	-20d																					

Start date	15DEC20
Must finish date	30APR23
© Primavera Systems, Inc.	

CONSTRUCTION PROGRAMME


- Early bar
- Progress bar
- Critical bar
- ◆ Start milestone point
- ◆ Finish milestone point

Date	Revision	Checked	Approved
28DEC21		ZYW	TSL

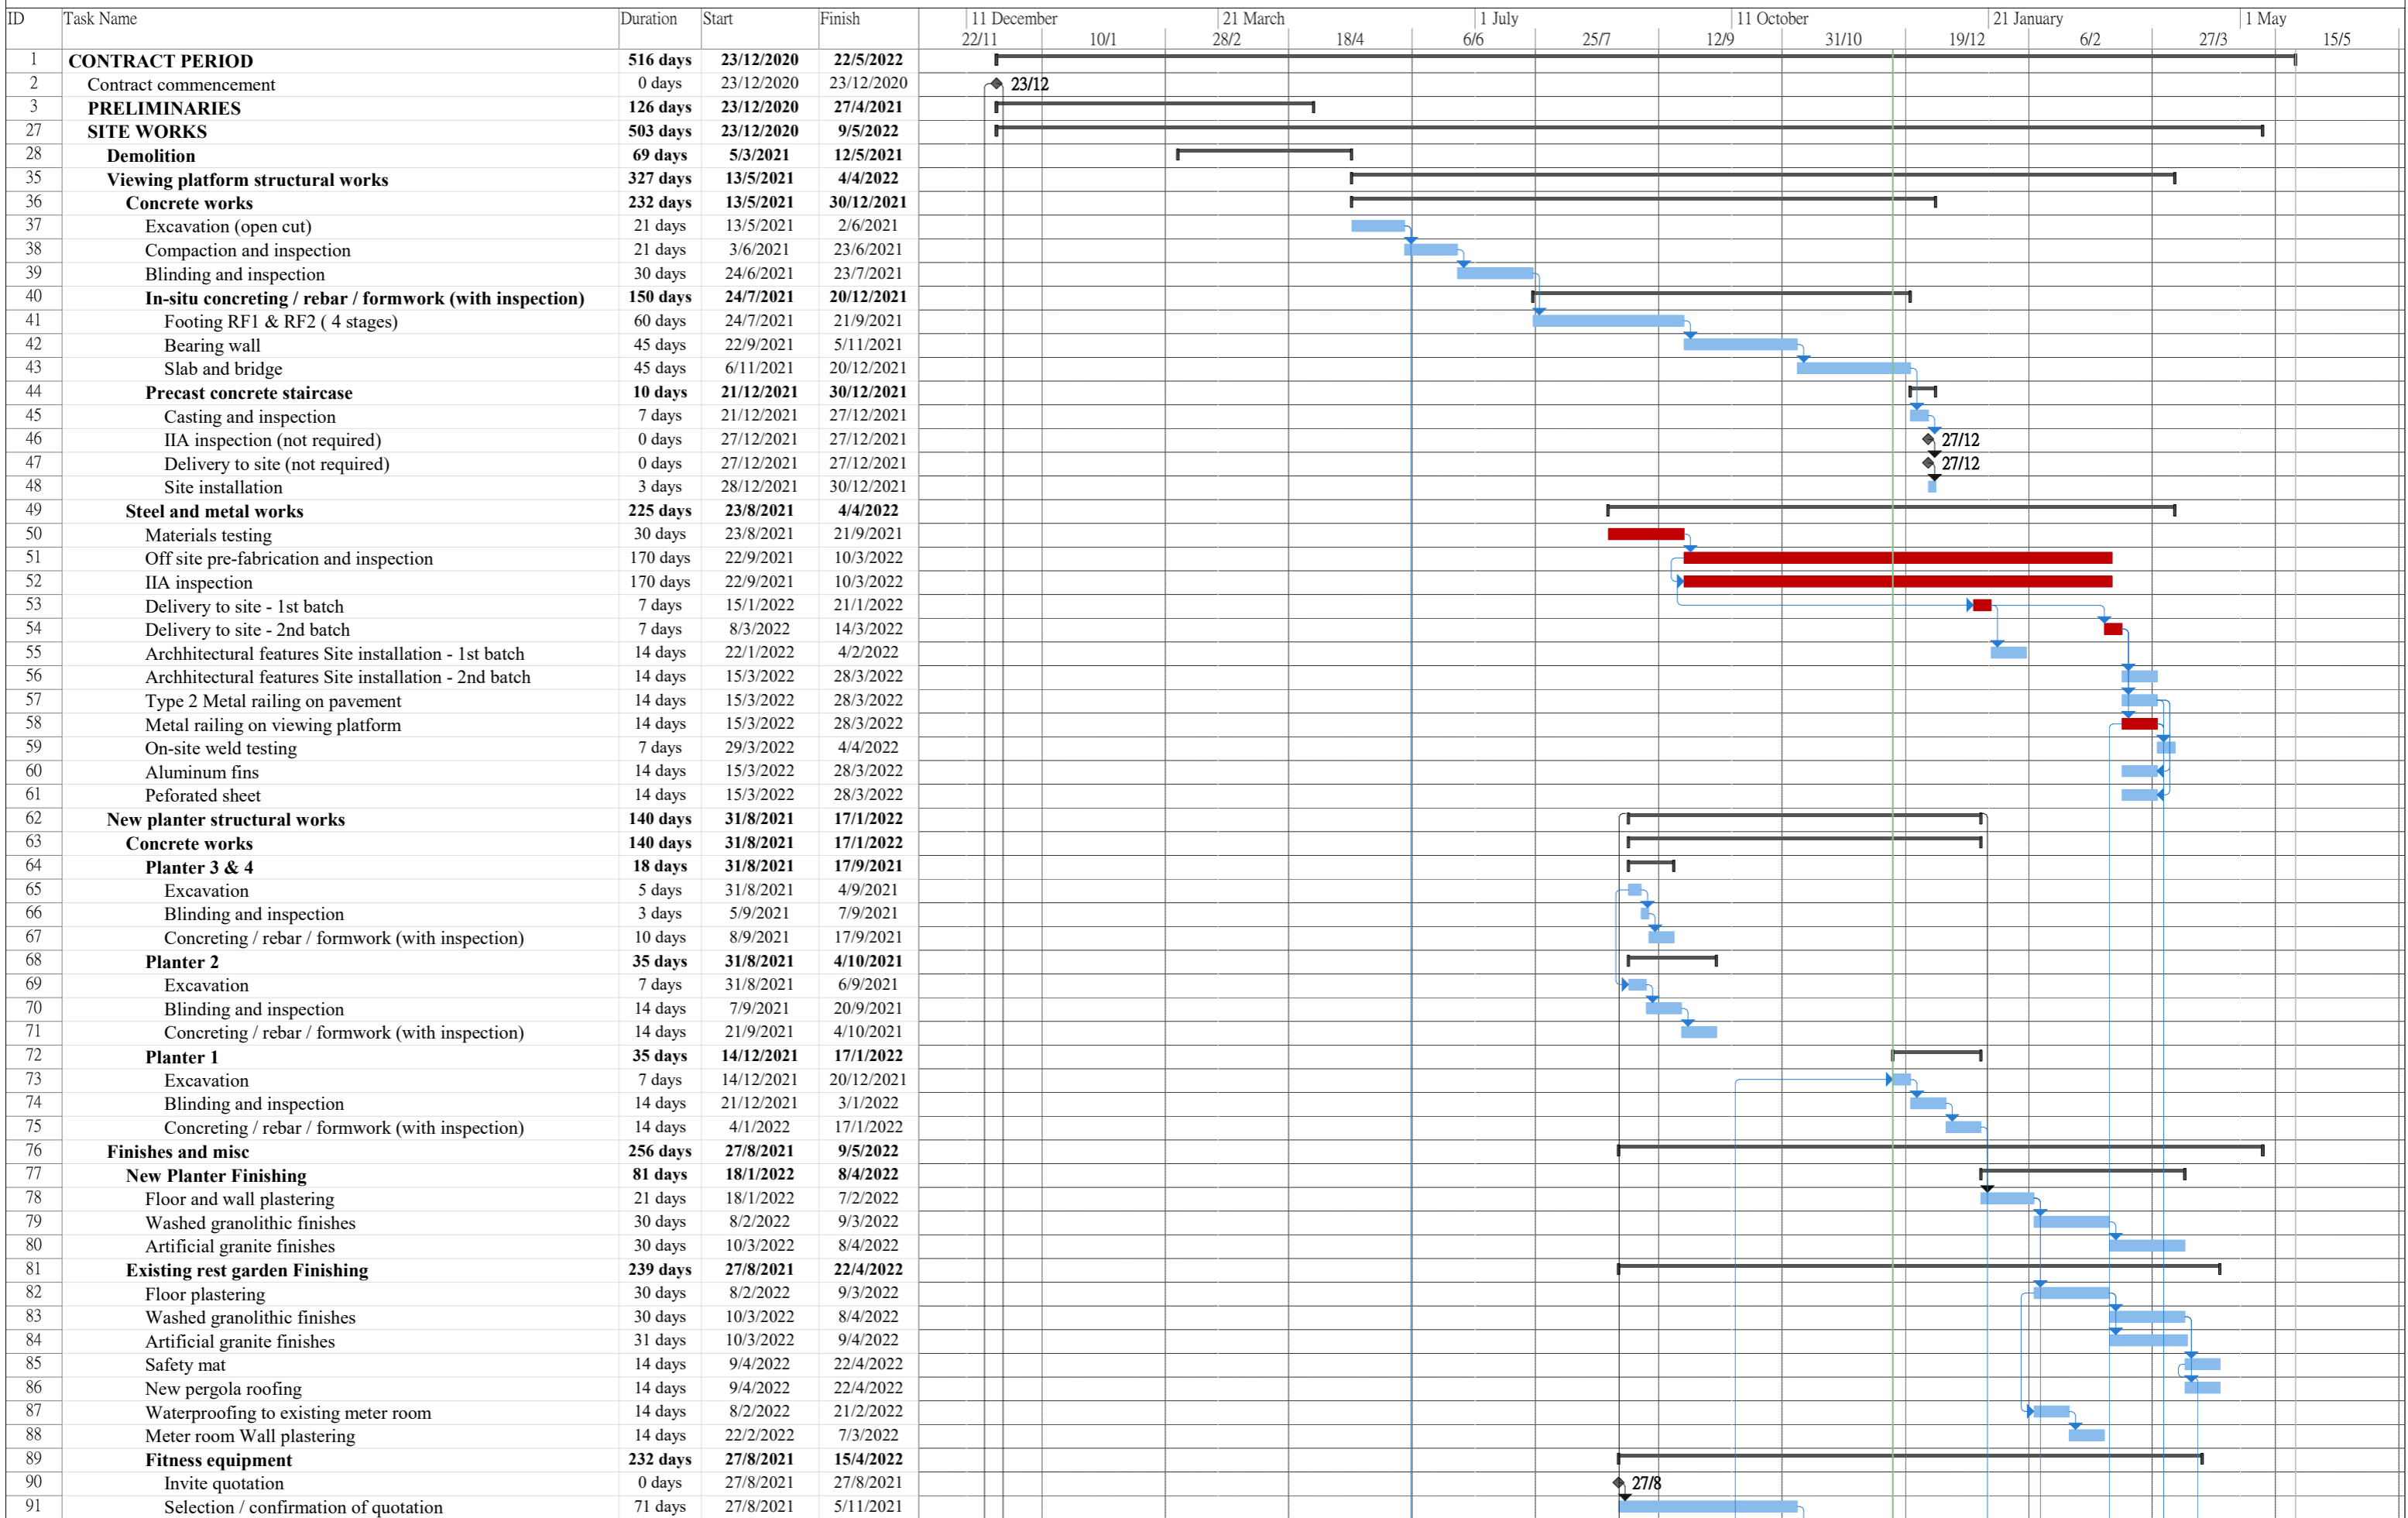

Project: SSJ521- LeiYuMun const p
 Date: 14/12/2021

..... Critical Split
 Task
 Split
 ◆ Milestone
 Summary
 Project Summary
 Critical
 Manual Progress
 —

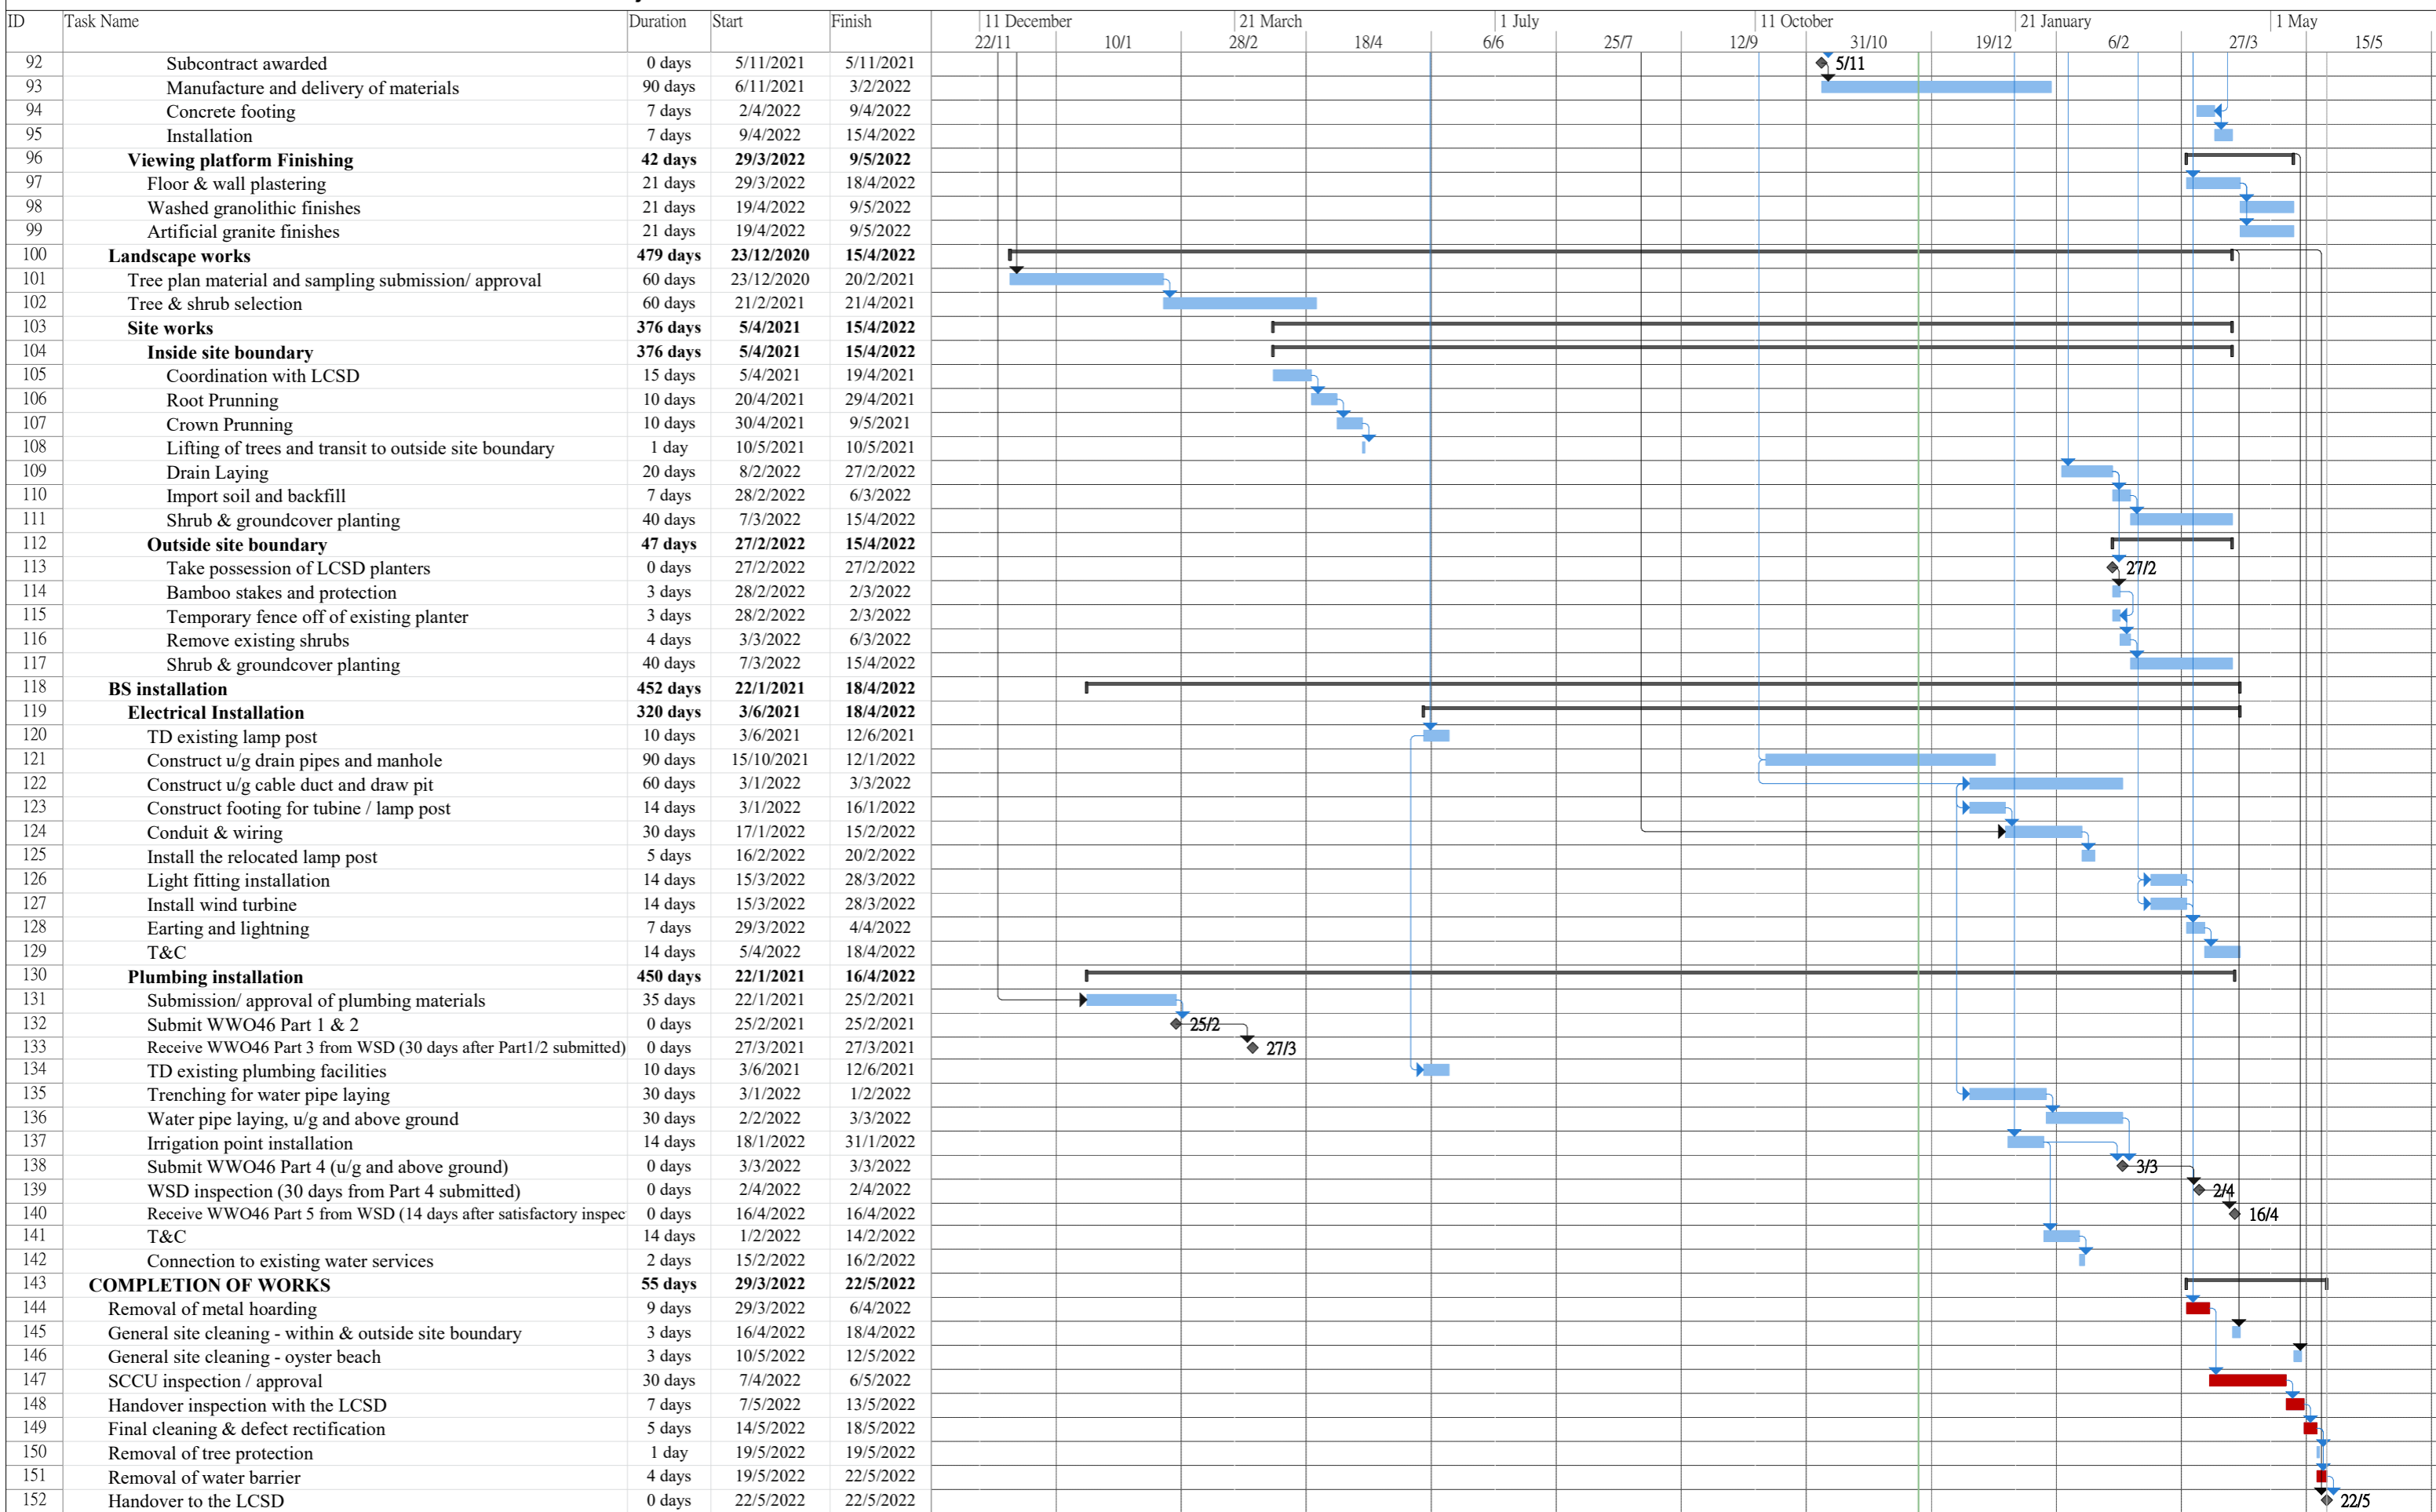

Project: SSJ521- LeiYuMun const p Critical Split Task Split Milestone Summary Project Summary Critical Manual Progress
